

## Instructions

Please download this Word document (available on the Industrial Commission/Outdoor Heritage Fund Program website at <http://www.nd.gov/ndic/outdoor-infopage.htm> ) to your computer and provide the information as requested. You are not limited to the spacing provided. After completing the report, save it and attach it to an e-mail and send it to [outdoorheritage@nd.gov](mailto:outdoorheritage@nd.gov) AND print it and mail it to: North Dakota Industrial Commission, ATTN: Outdoor Heritage Fund Program, State Capitol – Fourteenth Floor, 600 East Boulevard Ave. Dept. 405, Bismarck, ND 58505. If you are unable to scan attachments, mail them with your paper copy of the report. You will be sent a confirmation by e-mail of receipt of your report and attachments.

### Outdoor Heritage Fund Status and Final Report Form/Guidelines

This report is used to show progress of grant projects funded through the Outdoor Heritage Fund. Status Reports and the Final Report must be submitted as required in Contract.

Contract Number	Report Date	Period Covered by Report (xx/xx/xx to xx/xx/xx)
007-093	July 11, 2019	6/01/2019 to 7/12/2019

Project Name  
**O-M-G Grassland Improvement Project**

Project Sponsor Name  
**Oliver, Morton & Grant County Soil Conservation Districts**

Responsible Official (Last, First Middle)	Responsible Official's Title
<b>Schily, Connie</b>	<b>Grant Co. SCD Manager</b>

Project Sponsor Address  
**103 Dakota St., PO Box 257**

City	State	Zip Code	Telephone Number
<b>Carson</b>	<b>ND</b>	<b>58529</b>	<b>(701) 622-3381 ext. 3</b>

#### Financial Update

Please provide the following information regarding the funding for your project based on the contract award:

#### Funds Spent this Reporting Period

(As appropriate please provide copies of receipts for purchases)

Match Funding \$32,558.76

In-kind Funding \$ 1,780.85

**OHF Funding Requested for Reimbursement \$48,838.14**

**Total Funding Expended for this Reporting Period \$ 83,177.75**

#### Total Funds Spent to Date

Match Funding \$313,571.57

In-kind Funding \$ 29,889.37

**OHF Funding Received and Requested for Reimbursement \$470,357.39**

**Total Funding Expended to Date \$813,818.33**

#### Balance of Grant Funds

Match Funding \$286,428.43

In-kind Funding \$29,889.37

**OHF Funding still to be Requested \$429,642.61**

**Total Funding to be Expended on this Project \$1,500,000.00**

Do you anticipate needing to request a grant extension    If yes, please explain?

Yes     No

Work Completed during Period Covered by Report:

(This information will be posted on the Outdoor Heritage Fund/Industrial Commission website)

Seven producers completed practices during this time period.

Oliver Co. SCD submitted one payment application for one rural water hookup for a total cost of \$3382.00 and 600 feet of pipeline at a cost of \$6387.30.

Grant Co. SCD submitted three payment applications including 140.12 acres of pasture/hayland plantings at a cost of \$5319.86, a 2000 gal. livestock watering tank for \$2790.42, a 3000 gal. water holding tank for a solar system at a cost of \$3686.66, 5476 ft. of pipeline at a cost of \$13,631.35, a well upgrade to accommodate the pipeline at a cost of \$3884.83 and a 2000 gal. livestock watering tank at a cost of \$2890.87.

Morton Co. SCD submitted three payment applications including 3 livestock watering tanks costing \$3856.86, 15,433.74 ft. pipeline totaling \$31,597.24 and one well for \$6214.08.

(See attached photos and documentation).


A meeting is scheduled for the last week of July to review existing contracted obligations and to determine if an extension of the project is necessary to utilize remaining dollars.

Photos of work completed are welcome (If appropriate, please submit photos of key elements of the project completed or in progress during reporting period) Do not exceed five photos per project report.


Signature of Responsible Official

*Connie Schuly* 7-11-2019

The project reports shall be provided to the Commission in both electronic and hard-copy formats with permission for unrestricted distribution. The electronic versions shall be in a suitable format for posting on the Outdoor Heritage Fund/Commission website.

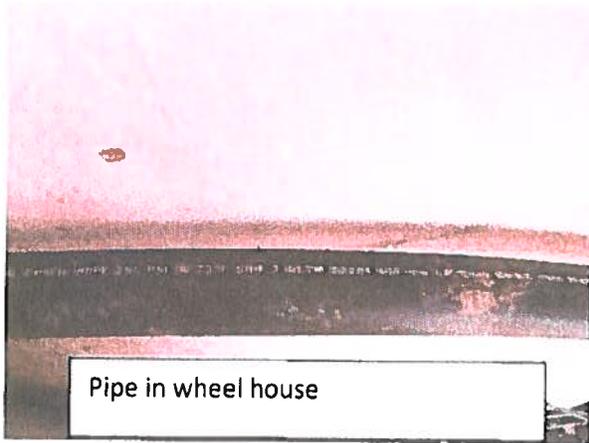


Pipe in wheel house

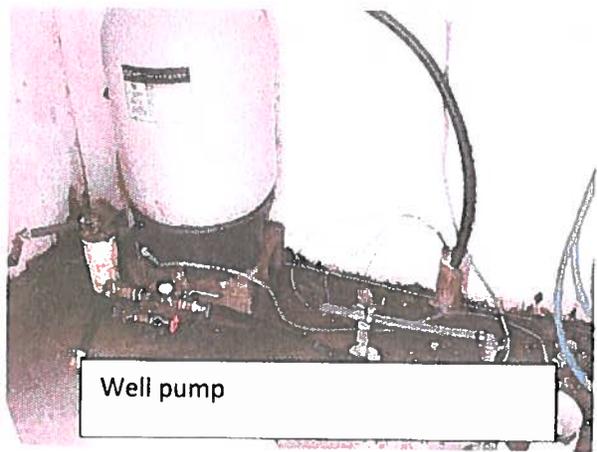


Well pump




Pipeline heading out to tank




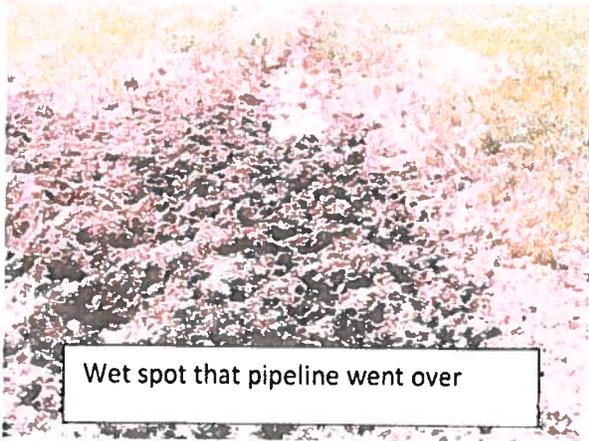

Wet spot that pipeline went over

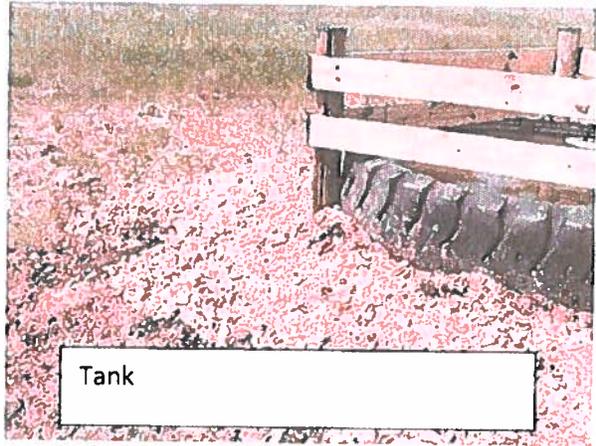

Tank

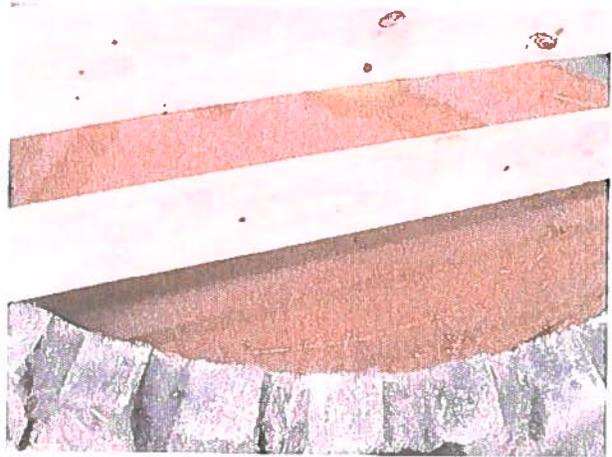

Wildlife escape ramp






Wilcox pasture/hayland planting 70.7 acres




Wilcox pasture/hayland planting 70.5 acres




Wildlife escape ramp tank section 8

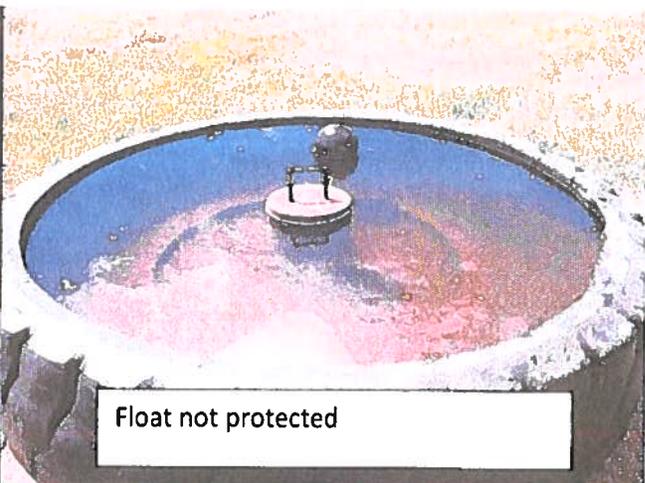


Float not protected

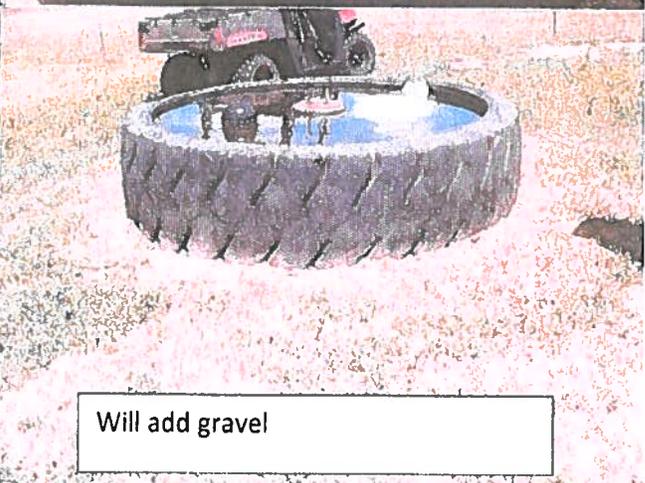

Will add gravel

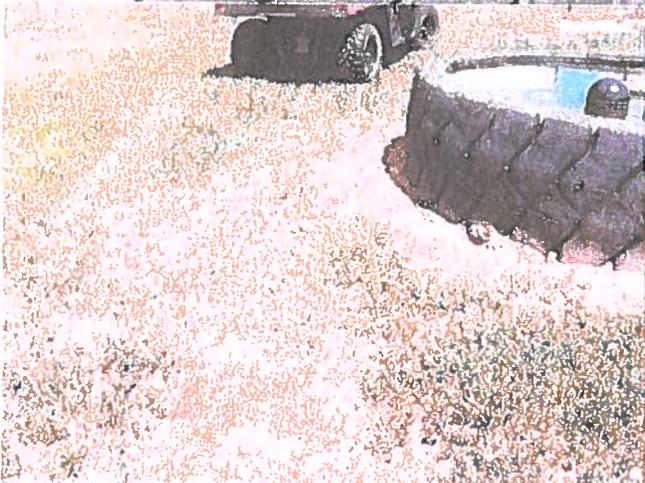

None cost shared fence

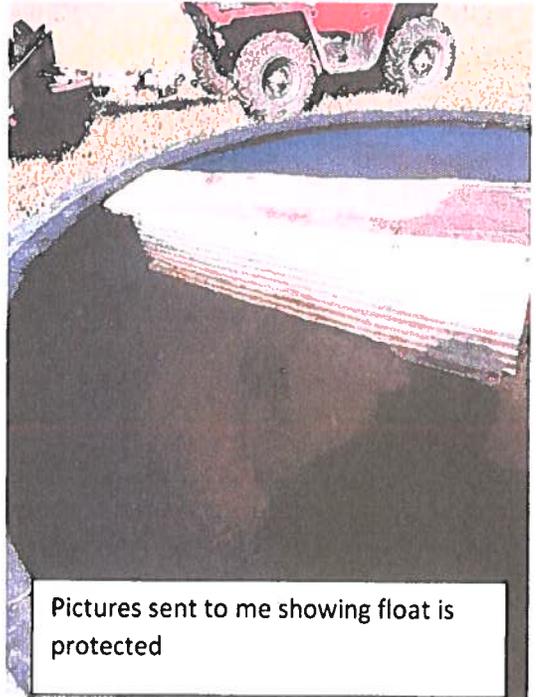

Pictures sent to me showing float is protected



Dawson solar panel, storage tank and livestock drinking tank




Rural water tap section 25





Trenched pipeline heading east from tap to tank



Pipeline heading east one section 25

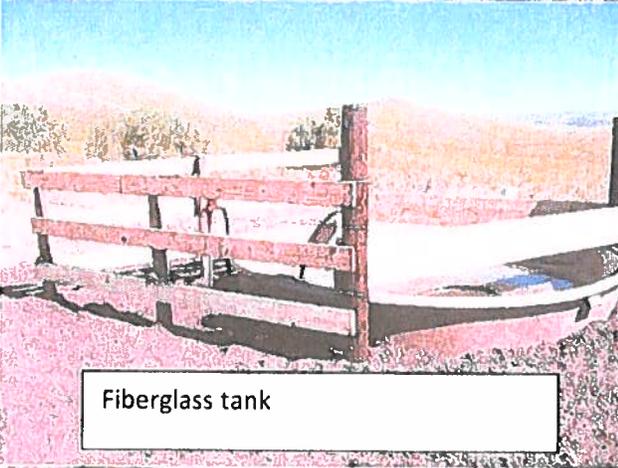


Fiberglass tank

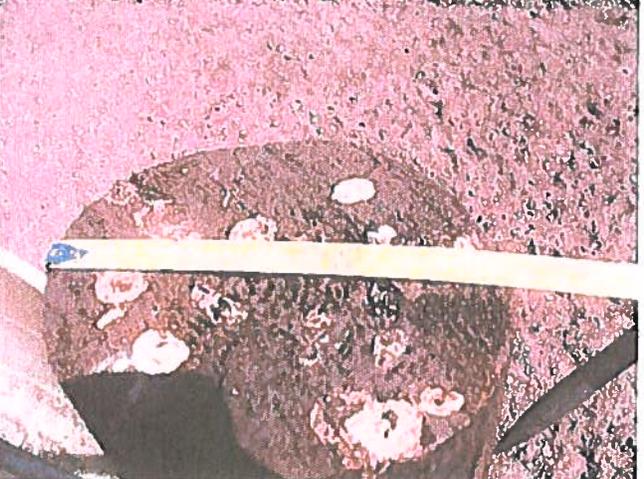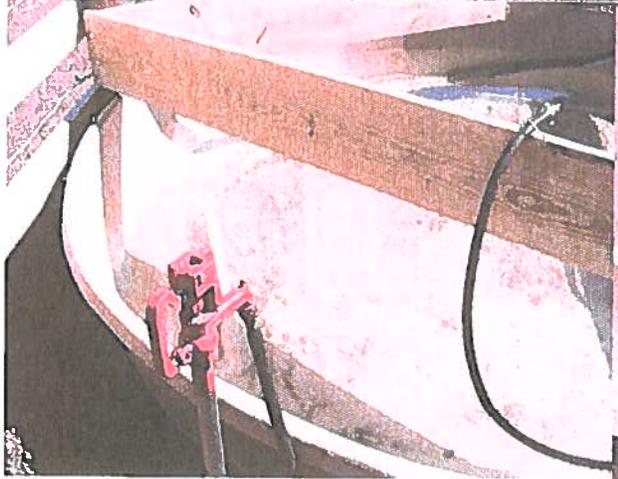



Ruscheinsky pipeline

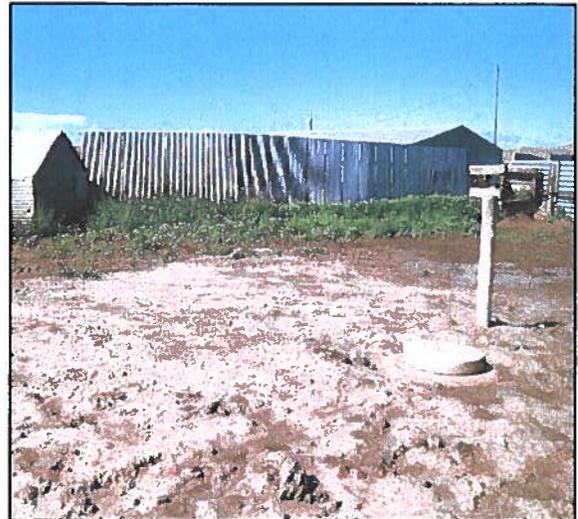

Ruscheinsky well



Ruscheinsky tank gravel



Ruscheinsky Tank brasing
